DRAFT FOR DISCUSSION PURPOSES 1/12/02

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 1 | **EHC Human Exposure Pilot** | **238 days** | **Thu 1/31/02** | **Tue 12/31/02** | |
| 2 | Draft Report target Ready for March SAB mtg | 0 days | Thu 1/31/02 | Thu 1/31/02 3/28/02 | |
| 3 | Ames Test 3 mos. | 0 days | Fri 5/31/02 | Fri 5/31/02 | |
| 4 | Final Report | 0 days | Fri 6/28/02 | Fri 6/28/02 | |
| 5 | **Publications** | **238 days** | **Thu 1/31/02** | **Tue 12/31/02** | |
| 6 | ETS | 0 days | Thu 1/31/02 | Thu 1/31/02 | |
| 7 | Cigarette Burn Time | 0 days | Fri 5/31/02 | Fri 5/31/02 | |
| 8 | Study Design and Smoking Behavior | 0 days | Mon 9/30/02 | Mon 9/30/02 | |
| 9 | Exposure Biomarkers | 0 days | Thu 10/31/02 | Thu 10/31/02 | |
| 10 | Potential Harm Biomarkers | 0 days | Thu 10/31/02 | Thu 10/31/02 | |
| 11 | Mutagenicity | 0 days | Tue 12/31/02 | Tue 12/31/02 | |

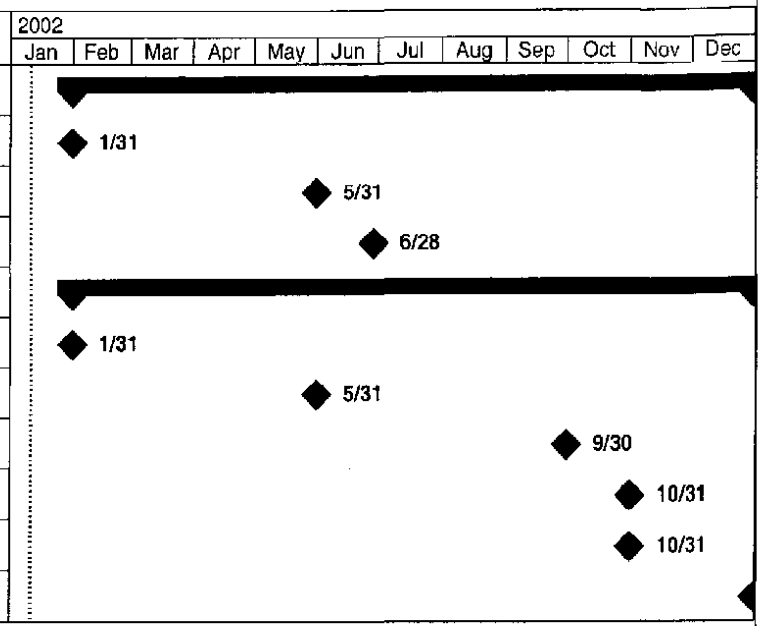


2 SAB meetings → target

* Mutmic / Ames Validation → end of January

Dependencies:
Final results/publications
↳ poster (4 wks with data)
↳ manuscript: 3 mos. (to submission)

*Biologic validation of HPMA, transmuconic acid: 5-6 wks 1/21/02 - 4 wks duration
Report - 4 wks FS validation

Project: Pilot
Date: Fri 1/11/02

Task | Split | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Split | Rolled Up Milestone | Rolled Up Progress | External Tasks | Project Summary



PM3006787442

Source: https://www.industrydocuments.ucsf.edu/docs/lymx0001
